MODULE 45 · FOUNDATIONS - ALL DOMAINS

# Case study: Project Lantern end to end

One extended case and ten linked questions across all three domains, including an exhibit, in the format the exam's case-study section uses.

DOMAIN Cross-domain  EXAM WEIGHT All domains  MODULE 45 of 49

admin@sthithapragna.com

# Map the case once. Then hunt for the one detail each question turns on.


admin@sthithapragna.com

# The case: Northgate Health and Project Lantern

| ITEM | DETAIL |
|---|---|
| Organisation | Northgate Health: six community clinics; consensus-driven and cautious |
| Project | Replace patient booking with an app, kiosks and a new booking system |
| Approach | Hybrid: predictive for network, kiosks and data migration; Scrum for the app |
| Duration and budget | Fourteen months; a controlling PMO; monthly steering committee |
| Main benefit | Missed appointments down by a quarter within a year of the last go-live |
| Rollout plan | Pilot clinic live in month 6; one clinic a month after that |

ON THE EXAM

Note the approach: hybrid. Predictive answers fit the kiosks and migration; agile answers fit the app.

# The people

| ROLE | WHO |
|---|---|
| Sponsor | Dana, the new chief operating officer, appointed in month 5 |
| Project manager | Sam, who has authority up to 5 percent on cost and 2 weeks on schedule |
| Product owner | Priya, from the patient access team |
| Scrum master | Luis, for the app team of seven developers |
| Benefit owner | The head of patient access |
| Other stakeholders | Clinic managers, reception staff, a union representative, the IT operations lead |

ON THE EXAM

Note who owns what: Priya owns the backlog order; Dana owns the business case; Sam's tolerances are stated.


# Where things stand at month 8

| AREA | STATUS |
| --- | --- |
| Rollout | Pilot clinic live since month 6; clinic 2 went live this month |
| Predictive work | CPI 0.94 and SPI 0.97; the governance threshold for escalation is 0.92 |
| App release | Planned to finish in 3 more sprints; see exhibit A |
| Clinic 2 | Reception staff slower than before, frustrated, and using paper notes alongside the app |
| Risks | The kiosk supplier is on a firm fixed price contract; a planned response exists for late kiosks |
| Data | Clinic 3's migration rehearsal is next week; the error threshold is 2 percent |

ON THE EXAM

Numbers here matter later: the 0.92 threshold, Sam's tolerances, and the 2 percent error threshold.

# Lantern app: release burnup

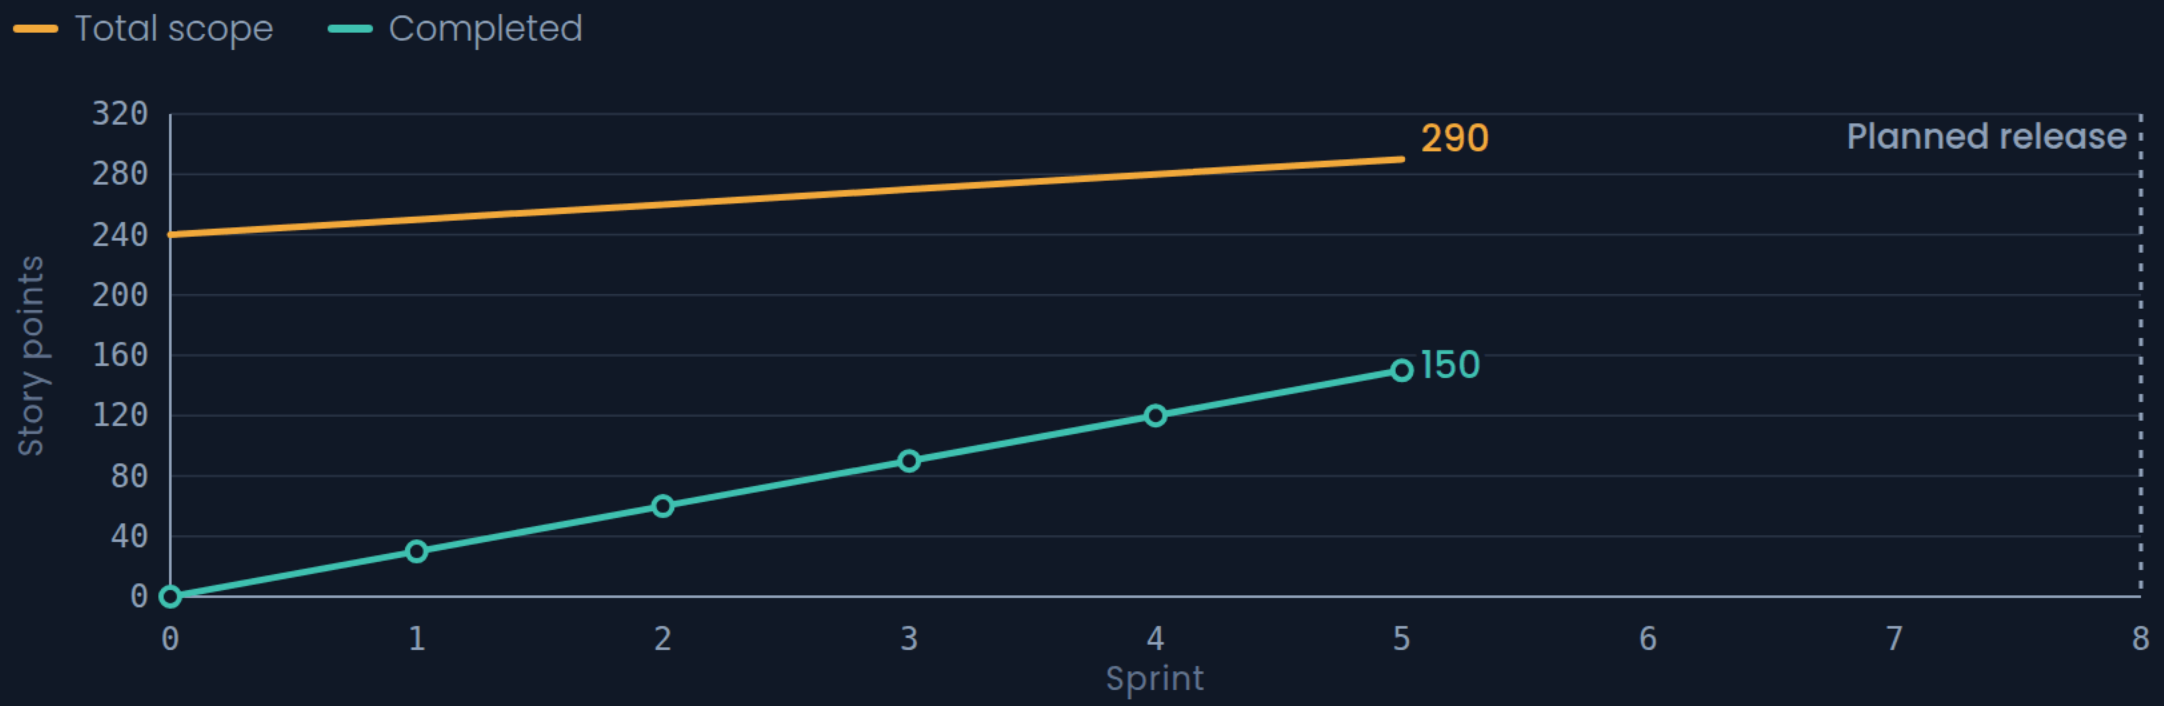

> In her first steering meeting, Dana, the new sponsor, asks Sam to take the remaining four clinics live together in month 10, instead of one a month, to 'finish faster'.
>
> Clinic 2 is still settling in, and the culture is cautious.

## What should Sam do FIRST?

A Agree, and re-plan for a combined go-live in month 10.

B Decline, because the approved plan is one clinic a month.

C Escalate Dana's request to the portfolio board.

D Assess the impact on readiness, risk and support with the team and clinics, and present options to Dana.

◆ PAUSE AND DECIDE

## What should Sam do FIRST?

A Agree and re-plan.

*Acts before understanding the risk to readiness and support.*

B Decline.

*The sponsor owns such decisions; the plan can change through proper analysis.*

C Escalate above the sponsor.

*Goes over the sponsor's head on her own decision.*

D Assess impact; present options.

Understand and assess first; the sponsor then decides with evidence.

DRAWS ON

Modules 02, 13 and 39: a new sponsor's request is assessed and answered with options, not accepted or refused blind.


admin@sthithapragna.com

> Refer to exhibit A. The app team has completed 150 story points in five sprints. Total scope has grown to 290 points.
>
> The release is planned for the end of sprint 8.

**Based on the exhibit, which statement is most accurate?**

A The team's velocity is falling, so the release is at risk.

B Velocity is steady at 30, but scope growth means about 5 more sprints are needed, not 3.

C The release will finish on time at the current velocity.

D The team has completed about two thirds of the total scope.

◆ PAUSE AND DECIDE


admin@sthithapragna.com

## Based on the exhibit, which statement is most accurate?

A Velocity is falling.
*The completed line rises by a steady 30 each sprint.*

B Steady velocity; scope growth; about 5 sprints.
140 remaining / 30 = 4.7 sprints, against 3 planned.

C On time.
*Three sprints at 30 completes 90 of the 140 remaining.*

D Two thirds done.
*150 of 290 is about half, not two thirds. It reads the original 240 as the total.*

DRAWS ON

Module 29: a burnup separates steady progress from scope growth. Module 43: remaining work over velocity.

> Following on from question 2, the release date is tied to clinic 3's go-live, which the clinics have already planned staff rotas around.
>
> Priya, the product owner, says every item in the backlog is important.

## What should Sam do NEXT?

A Ask the team to increase its velocity to 47 points a sprint.

B Freeze all scope changes until the release.

C Help Priya reprioritise, for example with MoSCoW, so the release fits the date, and agree the approach with Dana.

D Move the release date without discussion, since scope has grown.

◆ PAUSE AND DECIDE

## What should Sam do NEXT?

A Demand higher velocity.

*A 57 percent jump on demand is unrealistic, and inflates points.*

B Freeze scope.

*Stops learning, and does not remove the 140 points already there.*

C Reprioritise with the PO; agree with the sponsor.

Fixed date, flexing scope: the PO decides what fits; the sponsor agrees.

D Move the date unilaterally.

*The date is tied to clinic rotas, and is not Sam's alone to move.*

DRAWS ON

Modules 19 and 20: with time fixed, scope flexes. MoSCoW breaks 'everything is important'.

> Three weeks after clinic 2 went live, its manager reports that reception staff are slower, frustrated, and keeping paper notes alongside the app. There are no serious defects.
>
> The clinic manager asks whether the old booking system could be switched back on.

## What should Sam do?

A Explain that a temporary dip is normal, and increase on-site support, quick fixes and feedback, without reversing the change.

B Switch the old system back on until staff are comfortable.

C Repeat the full classroom training for all reception staff.

D Ban paper notes so staff must use the app.

◆ PAUSE AND DECIDE

## What should Sam do?

**A** Normal dip: support, fixes, feedback.

Supports people through the transition, and learns from their notes.

**B** Switch back.

*Reverses a working change at its hardest point.*

**C** Repeat classroom training.

*People in the neutral zone need support at the desk, not a classroom.*

**D** Ban paper notes.

*Forces compliance, and hides what the notes reveal about the app's gaps.*

DRAWS ON

Module 39: the dip after go-live is transition. Support through it; the paper notes are feedback.

> The union representative, recorded in month 2 as 'unaware', writes to Sam. Staff have heard that self-check-in kiosks will change reception shift patterns, and they are worried about their hours.
>
> Nobody from the project has met the union representative yet.

## What should Sam do?

A Reply that shift patterns are a matter for human resources, not the project.

B Send the representative the project's communications plan.

C Escalate the letter to Dana, since it involves the union.

D Meet the representative to understand the concerns, involve staff in planning, and update the engagement plan.

◆ PAUSE AND DECIDE

## What should Sam do?

A Not the project's matter.

*The project's change is causing the concern. Deflecting builds resistance.*

B Send the communications plan.

*A document does not answer a worry about people's hours.*

C Escalate to the sponsor.

*Too early; nobody has even talked to the representative.*

D Meet, understand, involve, update.

Engages a stakeholder who moved from unaware towards resistant, early and directly.

DRAWS ON

Modules 12 and 13: resistance is information. Meet, understand, involve, and update the engagement plan.

> The monthly report for the predictive workstreams shows a CPI of 0.94 and an SPI of 0.97. Last month they were 0.95 and 0.98.
>
> Dana asks whether this needs a steering committee decision.

## What should Sam advise?

A. Both indices are above the 0.92 threshold, so no escalation is required; report the slight downward trend and keep monitoring.

B. Both indices are below 1, so the steering committee must decide on corrective action.

C. The project is on track, so the indices need not be reported.

D. Rebaseline the cost and schedule so both indices return to 1.

◆ PAUSE AND DECIDE

## What should Sam advise?

**A** Within threshold; report the trend; monitor.

Governance set 0.92. Both are above it, but the downward trend deserves attention.

**B** Below 1, so escalate.

*Escalation is triggered by the agreed threshold, not by 1.*

**C** Do not report.

*Honest reporting includes a worsening trend, even inside tolerance.*

**D** Rebaseline.

*Hides variance instead of managing it.*

DRAWS ON

Modules 27 and 31: escalate against the agreed threshold, and always report the trend honestly.

> Luis reports that two senior developers have argued about the app's architecture in the last three daily meetings. The arguments have become personal, and other developers now stay silent.
>
> Both developers are highly skilled, and the team respects them.

## What should happen?

A Sam decides the architecture question to end the argument.

B Remove one of the developers from the team.

C Luis meets them privately to separate the technical question from the personal friction, then helps the team decide the architecture together.

D Ban architecture discussions from daily meetings, and take no other action.

◆ PAUSE AND DECIDE

## What should happen?

A Sam decides.
*Forcing a technical decision that belongs to the developers.*

B Remove a developer.
*Disproportionate, and loses real skill and knowledge.*

C Private conversation; team decides together.
Addresses relationship conflict privately, keeps healthy task debate.

D Ban the topic only.
*Hides the conflict; the architecture still needs deciding.*

DRAWS ON

Modules 10 and 11: turn relationship conflict back into task conflict, then decide as a team.

> Clinic 3's migration rehearsal finds errors in 7 percent of patient records, against a threshold of 2 percent. A Pareto analysis shows two error types cause 80 percent of the errors.
>
> Go-live is in three weeks, and Dana is keen to keep the date.

## What should Sam do?

A. Go live as planned, and fix the records afterwards.

B. Fix the root causes of the two main error types, re-run the rehearsal, and go live only when errors are under the threshold.

C. Raise the error threshold to 7 percent.

D. Fix all error types equally, one record at a time.

◆ PAUSE AND DECIDE

## What should Sam do?

A Go live; fix later.

*Patient records wrong in live use: a quality and safety failure.*

B Fix the vital few causes; re-rehearse.

Pareto points to two causes; fixing them gives the best chance of the date.

C Raise the threshold.

*Changes the measure, not the quality.*

D Fix everything equally.

*Spreads three weeks thinly, and treats symptoms record by record.*

DRAWS ON

Module 28: Pareto for the vital few; root causes, not records. Quality before the date on patient data.

> A regional regulator publishes a proposal requiring patient booking data to be stored within the region from next year. The new booking system's hosting is currently outside the region.
>
> The proposal is out for consultation for three months.

## What should Sam do?

A Ignore it until the regulation is confirmed.

B Move the hosting into the region immediately.

C Assess the impact with compliance and IT, record it as a risk with options, and keep watching the consultation.

D Stop the remaining clinic go-lives until the regulation is final.

◆ PAUSE AND DECIDE


admin@sthithapragna.com

## What should Sam do?

A Ignore it.
*Loses months of preparation time on a likely obligation.*

B Move hosting now.
*A major, costly change before the rule is even final.*

C Assess, record as a risk, prepare options, watch.
Proportionate response to a proposed external change.

D Stop the go-lives.
*Halts all benefits for a rule that is still out for consultation.*

DRAWS ON

Modules 33, 36 and 40: a proposed rule is a risk. Assess it, prepare options, and keep scanning.

> At month 14, all six clinics are live and accepted, contracts are closed, and lessons are captured. Missed appointments are down 12 percent so far, against a 25 percent target due within a year.
>
> Dana asks Sam to close the project.

## What should Sam do?

A. Keep the project open until the 25 percent target is reached.

B. Close the project formally, with the final report showing benefit progress, and confirm the head of patient access will keep measuring it.

C. Close the project and stop tracking the benefit, since the outputs are delivered.

D. Report the project as a failure, since the target has not been met.

◆ PAUSE AND DECIDE


admin@sthithapragna.com

## What should Sam do?

A Stay open for the benefit.

*Benefits often arrive after closure; the project's work is done.*

B Close formally; hand benefit tracking to its owner.

Outputs accepted; benefit measured by the named owner after closure.

C Stop tracking the benefit.

*Loses the evidence of whether the project was worth it.*

D Declare failure.

*The target is due within a year of the last go-live, not at month 14.*

DRAWS ON

Modules 20 and 30: close when the work is accepted; the benefit owner measures what arrives afterwards.

One case, ten decisions, every domain. The same habits answered them all.


admin@sthithapragna.com
